

Project Updates

Stakeholders - October 10, 2018

VIRGINIA INTERNATIONAL GATEWAY



9/18/18

Wharf Extension

November 2018 completion




9/18/18

Wharf Extension

STS rails ready for installation



Fender installation underway

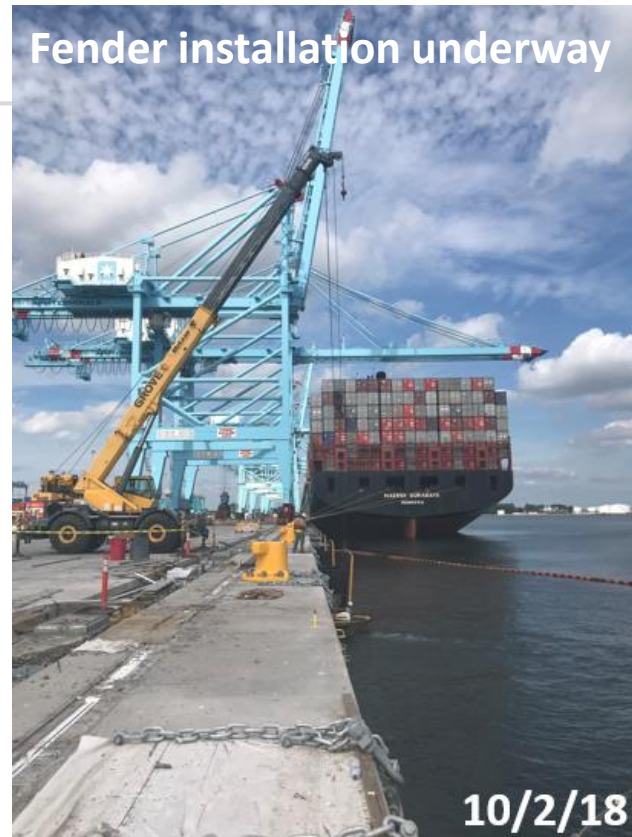



Rail Yard

South Rail Bundle operational


North Rail Bundle construction starts 11/1/18

9/18/18

Backus Aerial Photography

Rail Yard

CRMG cable trench for
North Rail Bundle

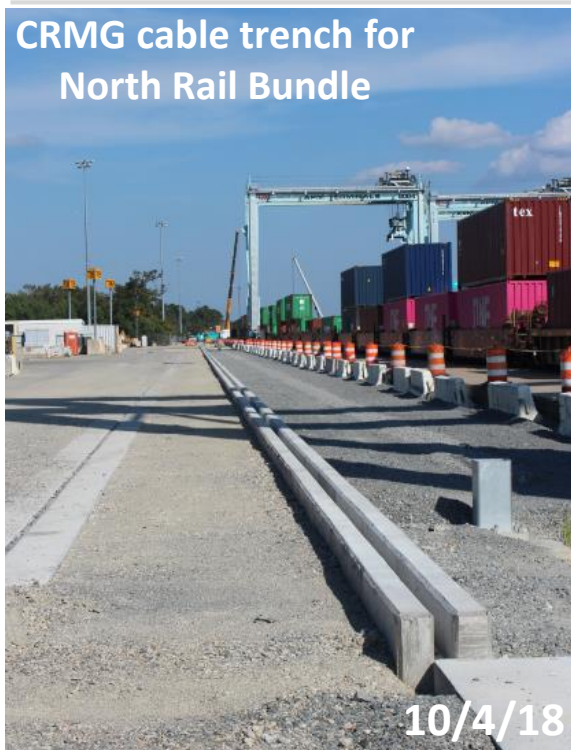


Train OCR foundations



Coning Cart/Grunt



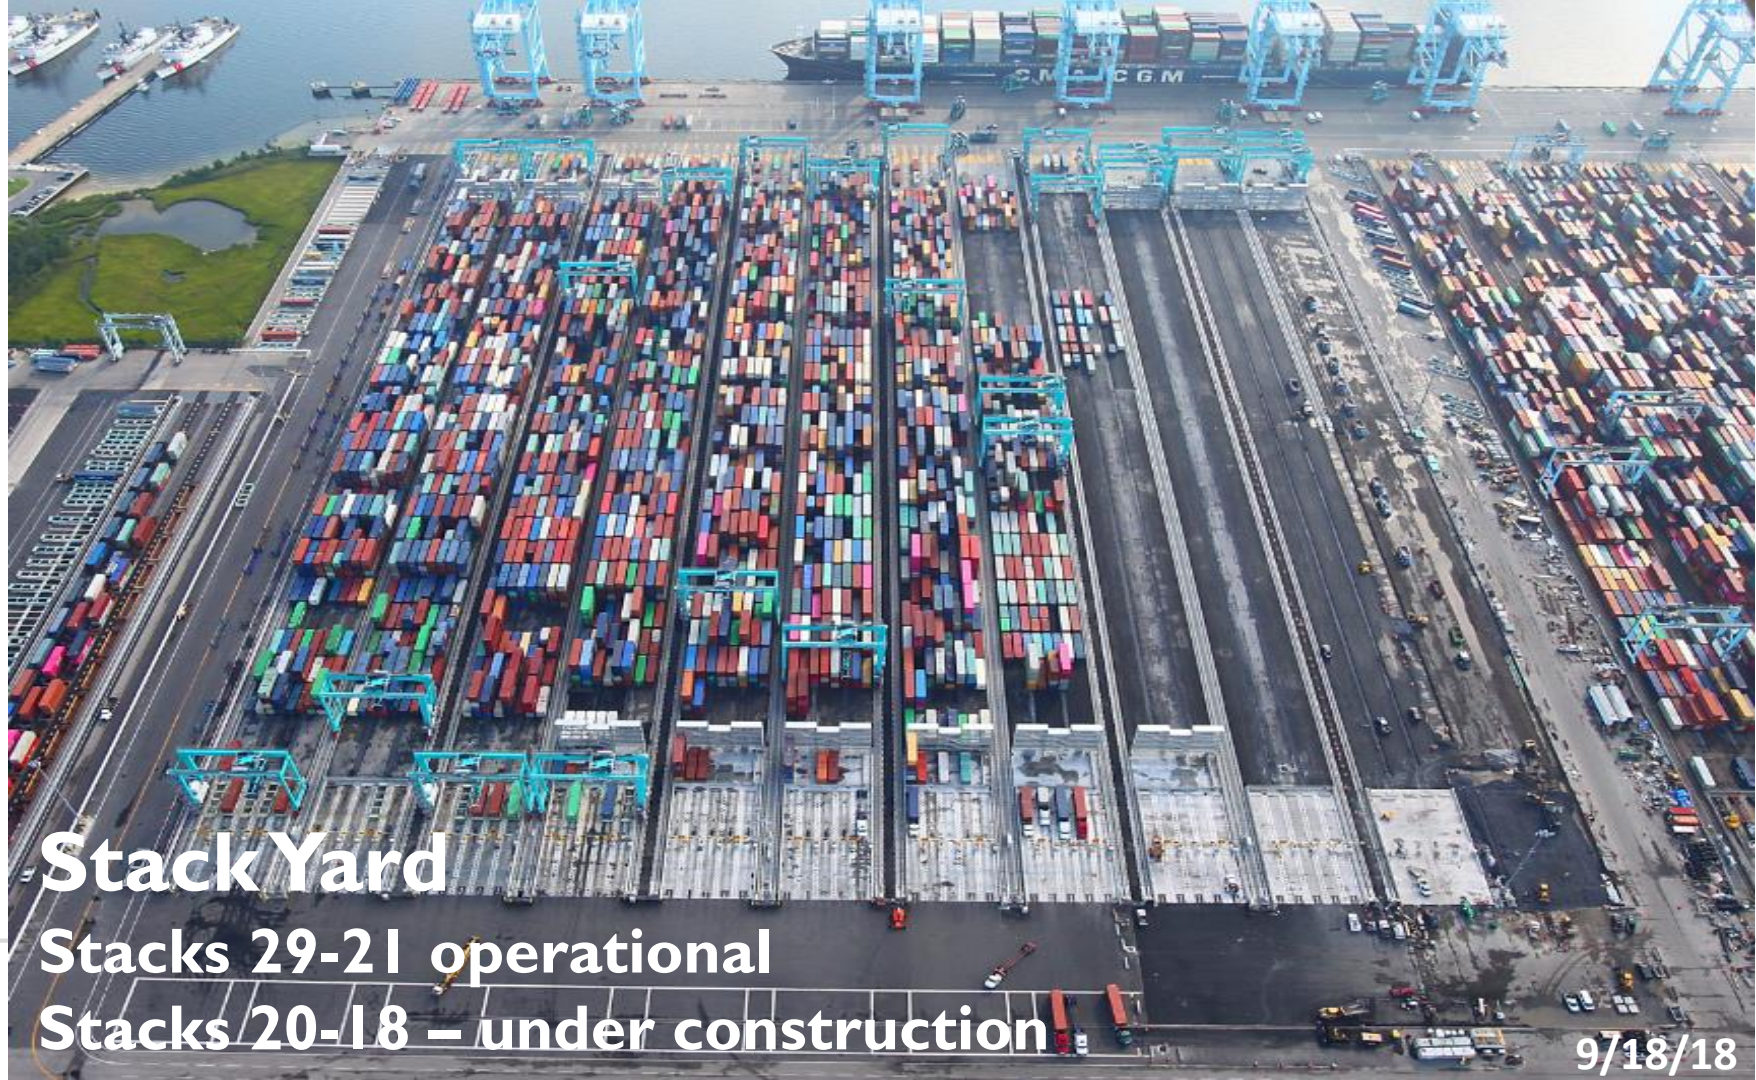

Stack Yard

Stacks 29-21 operational

Stacks 20-18 – under construction

9/18/18



Stack Yard

Stack 1 – new construction

Stack 2 & 3 – new reefer racks on the waterside and

RMG refurbishment underway

Backus Aerial Photography

9/18/18

Gate Project

4 new Inbound Gate Lanes in service



9/18/18

South NIT



9/18/18

Reekus Aerial Photography

SNIT – Phase I

First three new RMG stacks coming online soon

Nine more RMG stacks in Phase I




Backus Aerial Photography

9/18/18

SNIT – Phase I

Testing of the first 3 stacks

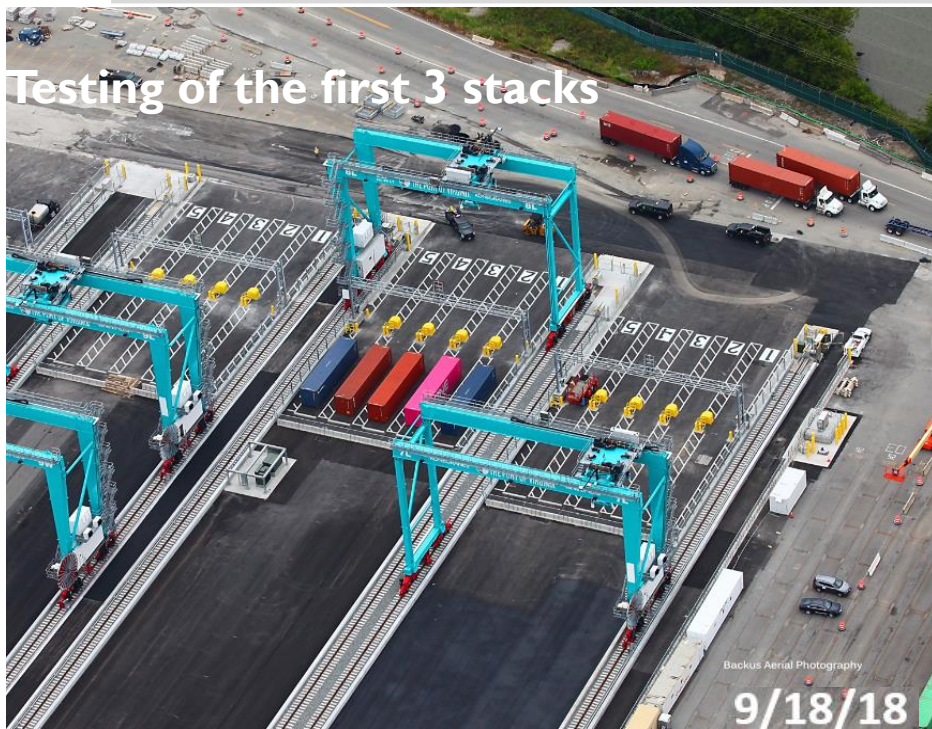

Landside reefer racks in stacks 13 - 16






SNIT Project | Second RMG Shipment



SNIT Project | Truck Staging Area



SNIT – First Commanded Move from N4

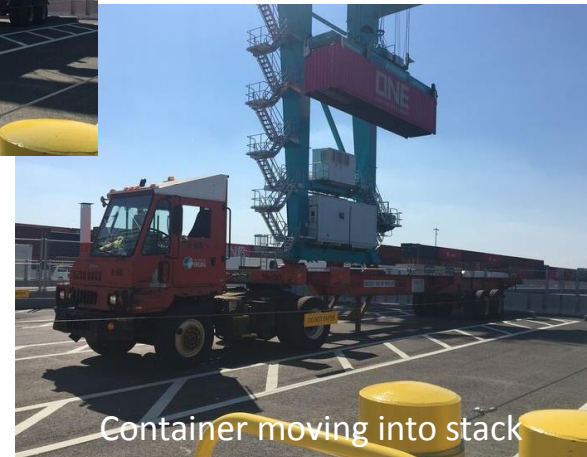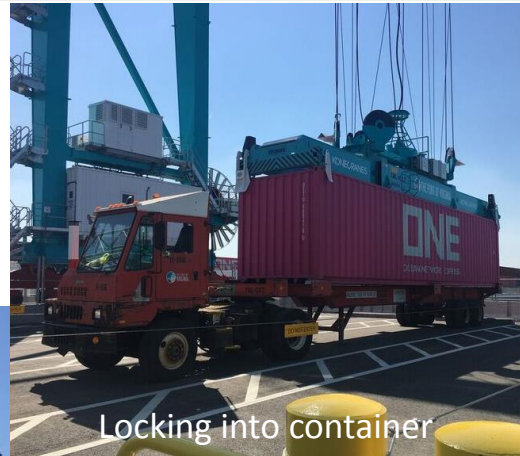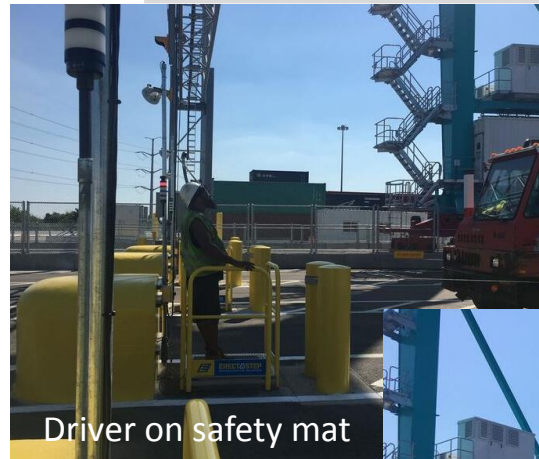

Thank you
